


Vessel : Mumbai Office	Risk Assessment No. : OFFC/RA-O/0004/2021
Category : Emergency Drills	Work Activity : D-003 - Deck Fire Drill

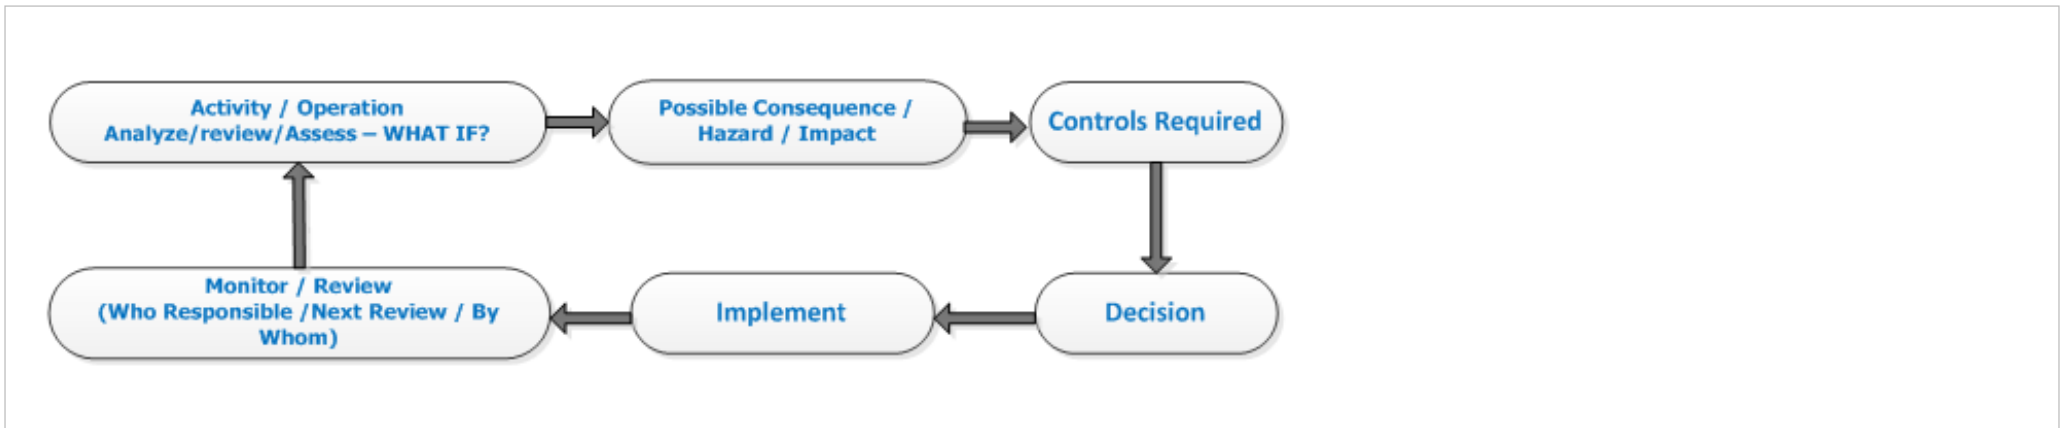

Name	Text	Value
Remote	Might occur every 10 to 20 years	1
Occasional	Might occur every 3 to 10 years	2
Likely	Might occur every 1 to 3 years	3
Frequent	Might occur more than once per year	4

Extent Of Consequences	Degree Of Impact
Trivial	1
Minor	2

Significant	3
Catastrophic	4

Activity/Operation	Hazard/Impact	Likelihood (L)	Degree Of Impact (D)	Irr [R=Lxd]	Sqa Procedure	Existing Control/Safeguard	Likelihood (L)	Degree Of Impact (D)	Rrr [R=Lxd]	Additional Control Req.?
Deck Fire Drill	Adverse Weather Conditions At Open Deck					Unsafe Conditions For Performing Such A Drill, If Fire Is On Main Deck, Alteration Of Course To Be Considered To Down Wind				
Deck Fire Drill	Adverse Weather Conditions At Open Deck					Unsafe Conditions For Performing Such A Drill, If Fire Is On Main Deck, Alteration Of Course To Be Considered To Down Wind				
Deck Fire Drill	Toxic Vapours Emmited From Cargo Hold Vents					Crew Should Be Gathered Within A Safe Range From Cargo Hold Vents, Only Crew With Scba Sets To Be Allowed Within The Scene Of The Fire				
Deck Fire Drill	Crew Exposed To Extreme Heat Or Sun Conditions					Unsafe Conditions For Performing Such A Drill				
Deck Fire Drill	Slippery Deck					Maintain Cleanliness Of Deck At All Times				
Deck Fire Drill	Crew Is Not Familiarized With Relevant Drill	4- Frequent	1- Trivial	4		Refer To 'Fire On Board Drill' Procedures. All Crew To Be Briefed And Well Familier Of Individual Duties. Ism Form B.7.30 To Be Complied With				
Deck Fire Drill	Handheld Vhf Units Not Charged					Dedicated Vhf Units To Be Used By Fire Parties To Be Identified And Marked. Location Of Same To Be Know To The Fire Party				
Deck Fire Drill	Fire Hoses And Nozzles Not Stowed In Proper Areas					All Fire Hoses And Nozzles To Be Properly Stowed As Per Fire Plan.				
Deck Fire Drill	Fireman'S Outfit In Poor Condition					All Crew To Be Familiar With The Checks To Be Carried Out Prior To Donning The Firman'S Outfit And Scba Sets				
Deck Fire Drill	Fire Extinguishers In Poor Condition And/ Or Not Properly Stowed					Maintenance Of Ffa Equipment To Be As Per Company Pms Policy				

Deck Fire Drill	Fatigue					Drill To Be Planned In Such A Way So As To Minimize Any Disturbance To The Rest Hours Of The Crew Involved.				
-----------------	---------	--	--	--	--	---	--	--	--	--

Contingency Measures										
-----------------------------	--	--	--	--	--	--	--	--	--	--

Master :			Chief Engineer :				Date : 13/Oct/2021			
Chief Officer :			2nd Engineer :							

Approver	Date Sent	Status	Approver Remarks	Date Actioned	
Vikram Puri	13/Oct/2021	Approved	please approve	13/Oct/2021	Reject
